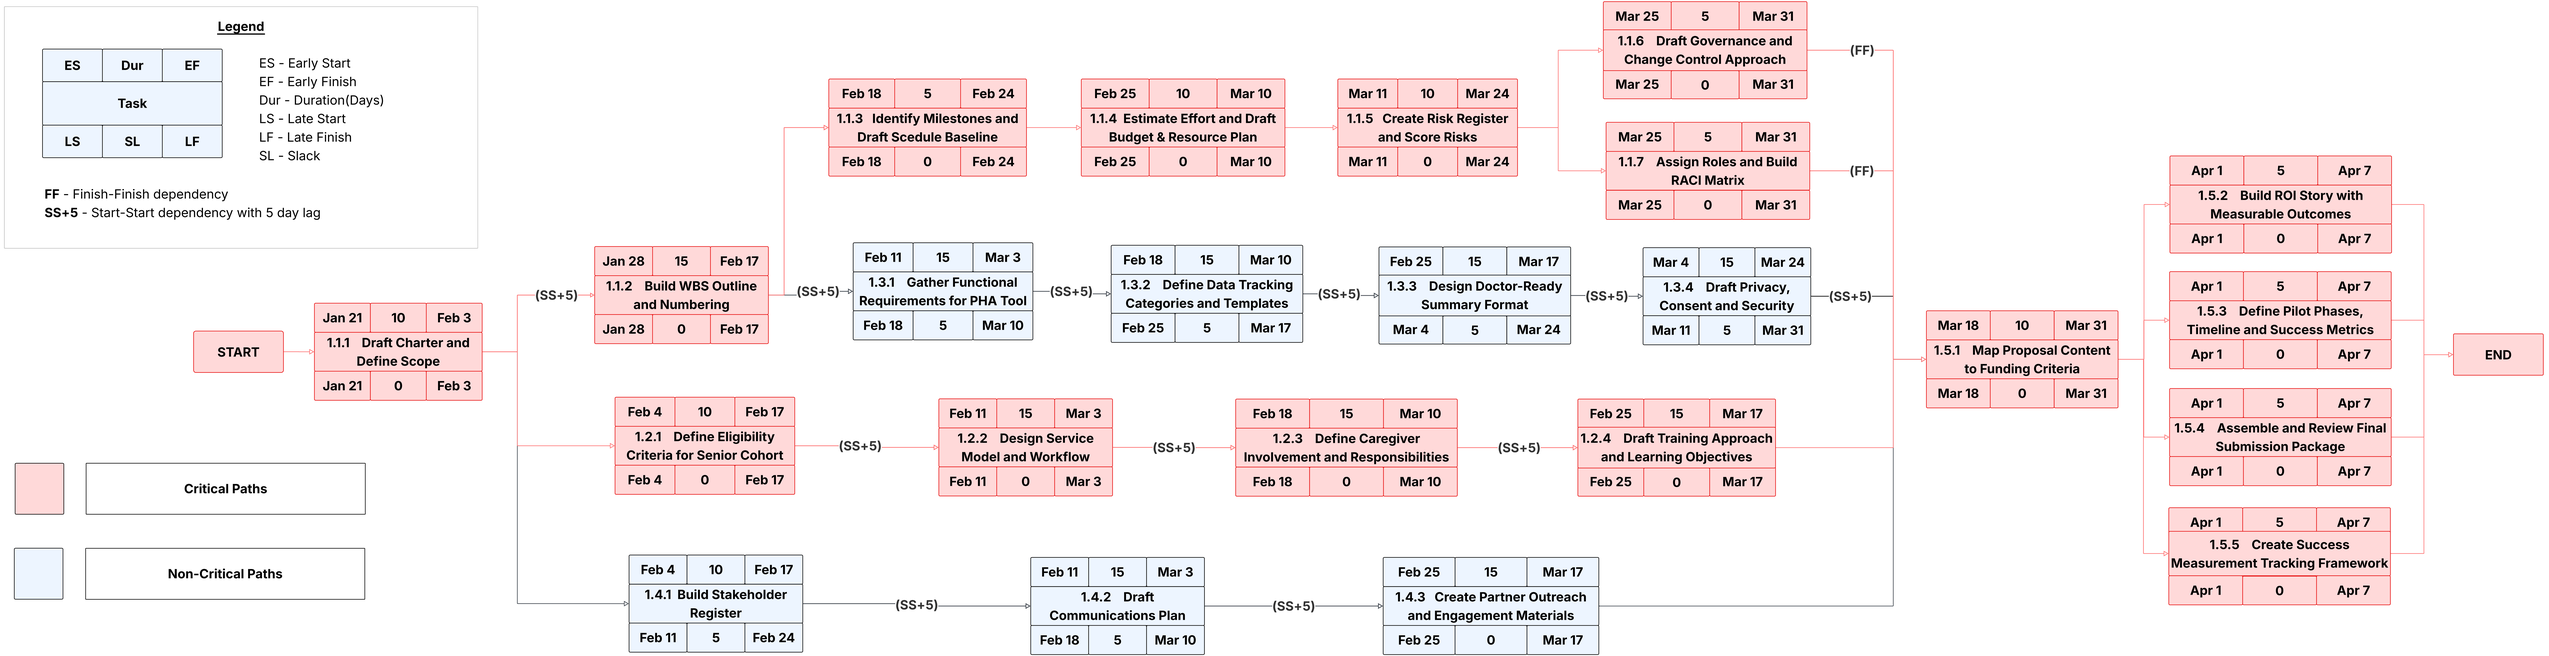
Legend
ES | Dur | EF
Task
LS | SL | LF
ES - Early Start
EF - Early Finish
Dur - Duration(Days)
LS - Late Start
LF - Late Finish
SL - Slack
FF - Finish-Finish dependency
SS+5 - Start-Start dependency with 5 day lag
Critical Paths
Non-Critical Paths
START
Jan 21 | 10 | Feb 3
1.1.1 Draft Charter and Define Scope
Jan 21 | 0 | Feb 3
(SS+5)
Jan 28 | 15 | Feb 17
1.1.2 Build WBS Outline and Numbering
Jan 28 | 0 | Feb 17
(SS+5)
Feb 18 | 5 | Feb 24
1.1.3 Identify Milestones and Draft Scedule Baseline
Feb 18 | 0 | Feb 24
Feb 25 | 10 | Mar 10
1.1.4 Estimate Effort and Draft Budget & Resource Plan
Feb 25 | 0 | Mar 10
Mar 11 | 10 | Mar 24
1.1.5 Create Risk Register and Score Risks
Mar 11 | 0 | Mar 24
Mar 25 | 5 | Mar 31
1.1.6 Draft Governance and Change Control Approach
Mar 25 | 0 | Mar 31
(FF)
Mar 25 | 5 | Mar 31
1.1.7 Assign Roles and Build RACI Matrix
Mar 25 | 0 | Mar 31
(FF)
Feb 11 | 15 | Mar 3
1.3.1 Gather Functional Requirements for PHA Tool
Feb 18 | 5 | Mar 10
(SS+5)
Feb 18 | 15 | Mar 10
1.3.2 Define Data Tracking Categories and Templates
Feb 25 | 5 | Mar 17
(SS+5)
Feb 25 | 15 | Mar 17
1.3.3 Design Doctor-Ready Summary Format
Mar 4 | 5 | Mar 24
(SS+5)
Mar 4 | 15 | Mar 24
1.3.4 Draft Privacy, Consent and Security
Mar 11 | 5 | Mar 31
(SS+5)
Feb 4 | 10 | Feb 17
1.2.1 Define Eligibility Criteria for Senior Cohort
Feb 4 | 0 | Feb 17
(SS+5)
Feb 11 | 15 | Mar 3
1.2.2 Design Service Model and Workflow
Feb 11 | 0 | Mar 3
(SS+5)
Feb 18 | 15 | Mar 10
1.2.3 Define Caregiver Involvement and Responsibilities
Feb 18 | 0 | Mar 10
(SS+5)
Feb 25 | 15 | Mar 17
1.2.4 Draft Training Approach and Learning Objectives
Feb 25 | 0 | Mar 17
Feb 4 | 10 | Feb 17
1.4.1 Build Stakeholder Register
Feb 11 | 5 | Feb 24
(SS+5)
Feb 11 | 15 | Mar 3
1.4.2 Draft Communications Plan
Feb 18 | 5 | Mar 10
(SS+5)
Feb 25 | 15 | Mar 17
1.4.3 Create Partner Outreach and Engagement Materials
Feb 25 | 0 | Mar 17
Mar 18 | 10 | Mar 31
1.5.1 Map Proposal Content to Funding Criteria
Mar 18 | 0 | Mar 31
Apr 1 | 5 | Apr 7
1.5.2 Build ROI Story with Measurable Outcomes
Apr 1 | 0 | Apr 7
Apr 1 | 5 | Apr 7
1.5.3 Define Pilot Phases, Timeline and Success Metrics
Apr 1 | 0 | Apr 7
Apr 1 | 5 | Apr 7
1.5.4 Assemble and Review Final Submission Package
Apr 1 | 0 | Apr 7
Apr 1 | 5 | Apr 7
1.5.5 Create Success Measurement Tracking Framework
Apr 1 | 0 | Apr 7
END
